LINCOLN COUNTY
SEPTIC SYSTEM PERMIT NO. NEW

ISSUED TO: Roy S. Long DATE: 7-12-83

ADDRESS: [redacted] PHONE:

ISSUED BY (sign.) John W Peterson, R.S.

INSPECTION BY (sign.) DATE:

(You must notify the Department of Environmental Health a minimum of 8 working day hours before backfilling the septic system, so that it can be inspected.)

CONTRACTOR: Marshall Warrington Rt 2 Troy

DESCRIPTION OF SYSTEM:

LOCATION OF PROPOSED SYSTEM Lot 77 Block I Angel Island


SEPTIC TANK 750 Min. gal. ABSORPTION AREA: 450 ft²

SEWAGE DISCHARGE — gal/day No. OF BEDROOMS 2

WATER SUPPLY SOURCE Community SOIL Silty loam SLOPE 0%-1%

INSTRUCTIONS: Construct a seepage bed as per lot layout & attached diagram. Slope of pipe in bed should be 0%. Construct a drywell for laundry graywater as per lot layout. Surround drywell ring with at least 1' of clean rock.

SKETCH OF LOT LAYOUT:

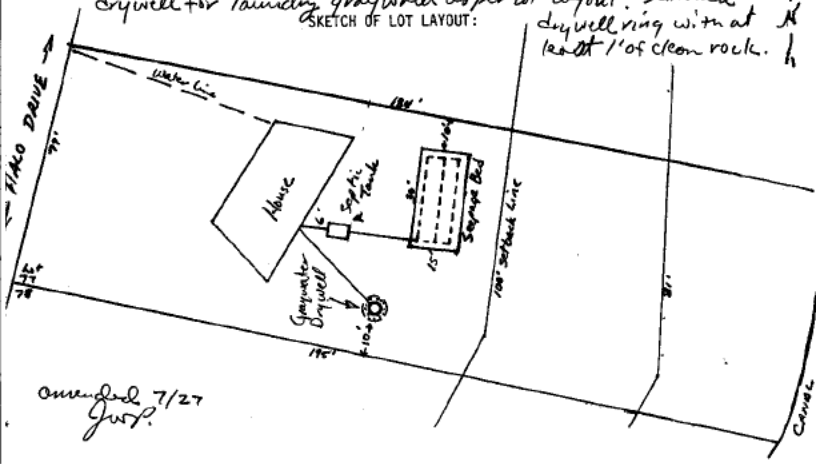

approved 7/27
JWP
