LINCOLN COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 07/18/2022 Expiration Date: 07/17/2023

Property Owner: Justin & Sue Haveman

Mailing Address: [redacted]

Telephone: [redacted] Email:

Installer: self License #:

Proposed Work: (Check One) ☒ New Installation ☐ Existing System

☐ Replace Drainfield ☐ Replace Tank ☐ Extension

Describe: Install two 95' laterals, 2' wide, using infiltrators. Gravity system.

Parcel Description:

Legal: Berger Lake Ph 3, Lot 12, S25 T37N R27W

Property Address: 250 Berger Ln Assessment Code: 53279

Approved Design Criteria:

# of Bedrooms: 2 Septic Tank Size: 1000 gallons Drainfield Size: 380 square feet

# of Laterals: 2 Length of Laterals: 95 Trench Depth: 24-36 inches

SYSTEM MUST INCLUDE INSTALLATION OF EFFLUENT FILTER AT SEPTIC TANK OUTLET!!

Special Instructions: Install system according to the lot layout, the Lincoln County Wastewater Treatment and Disposal Regulation, and Circular DEQ-4. ANY CHANGES MUST BE PRE-AUTHORIZED BY THE DEPARTMENT.

Issued By: *Kathi J. Hooper, R.S.*

NOTICE: The Department must be notified at least 3 business days (72 hours) prior to backfilling the system. Call 406-283-2442. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation Ch. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.

Closure Statement:

I, Robin Blumberg, have reviewed this system and found it to be in compliance with the approved design criteria and Lincoln County's Wastewater Treatment and Disposal Regulation.

Signed: Robin Blumberg *Date:* 4/26/23


✓ Lincoln County Health Department (LCHD) ____ Licensed Installer w/ approval of LCHD

DISCLAIMER

This permit is not a guarantee by the Department that the system will function properly for a prescribed period of time.

Modified Site Plan

Berger Lake Unit III
Water & Sewer plan 7-30-97.
Lincoln County.

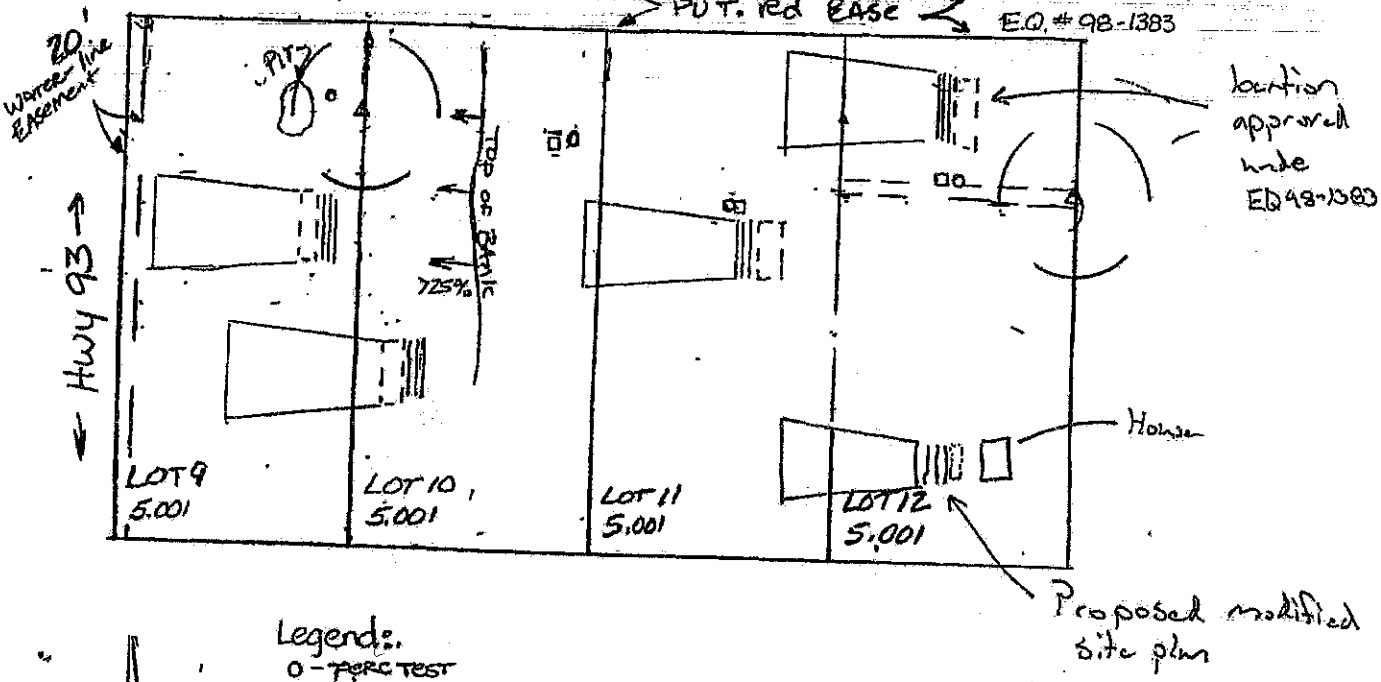

Legend:
- O - PERC TEST
- □ - TEST HOLE
- (Δ) WELL SITE W/100' ISOLATION ZONE
- ≡ - DRAINFIELD SITE
- - - - replacement AREA
- ▨ - MIXING ZONE

* ALL SITES NEARLY LEVEL

Scale 1"=200'

APPROVED
Montana Department of Environmental Quality
9/23/97
Permitting & Compliance Reviewer Date

APPROVED
Montana Department of Environmental Quality
Revlewer Date 6/13/2022
EQ#-98-1383

RECEIVED
JUN - 1 2022
MT DEQ PUBLIC WATER & SU

Drainfield sizing
LOT 9 = 3 trenches @ 65' w/10' spacing
LOT 10 = 11 11 @ 95' " "
LOT 11 = 3 trenches @ 65' w/10' spacing
LOT 12 = " " @ 95' " "

RECEIVED
SEP 12 1997
MT. DEPT. OF ENV. QUALITY
PERMITTING & COMPLIANCE DIV
