LINCOLN COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 12/23/2022 Expiration Date: 12/22/2023

Property Owner: James Hayford

Mailing Address: [redacted]

Telephone: [redacted] Email: [redacted]

Installer: Matt Sweeney/Sweeney Services License #: 48 (Flathead)

Proposed Work: (Check One) ☒ New Installation ☐ Existing System

☐ Replace Drainfield ☐ Replace Tank ☐ Extension

Describe: Level 2 system & gravelless pressure-dosed drainfield per DEQ COSA, EQ #08-1226

Parcel Description:

Legal: Parkside @ Fisher River, Lot 8, S14 T27N R28W, 4.795 acres

Property Address: 375 Rogers Mountain Loop, Libby Assessment Code: 56132

Approved Design Criteria:

# of Bedrooms: 3 Drainfield: 500 square feet Trenches: 36" wide, 18" deep

Per COSA: a 1500 gallon septic tank with effluent filter, one Advantex AX-20 Filter Pod, a 1000/500 gallon AX-recirculation tank, a 1000 gallon dose tank. O&M contract required.

Install system according to the lot layout, the Lincoln County Wastewater Treatment and Disposal Regulation, Circular DEQ-4, and the approved plans and specifications from Rowland Environmental Consulting Inc dated 12/26/07. ANY CHANGES MUST BE PRE-AUTHORIZED BY THE DEPARTMENT.

Issued By: *Kathi J. Hooper, R.S.*

NOTICE: The Department must be notified at least 3 business days (72 hours) prior to backfilling the system. Call 406-283-2442. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation Ch. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.

Closure Statement:

I, Kathi Hooper, have inspected this system and found it to be in compliance with the approved design criteria and Lincoln County's Wastewater Treatment and Disposal Regulation.

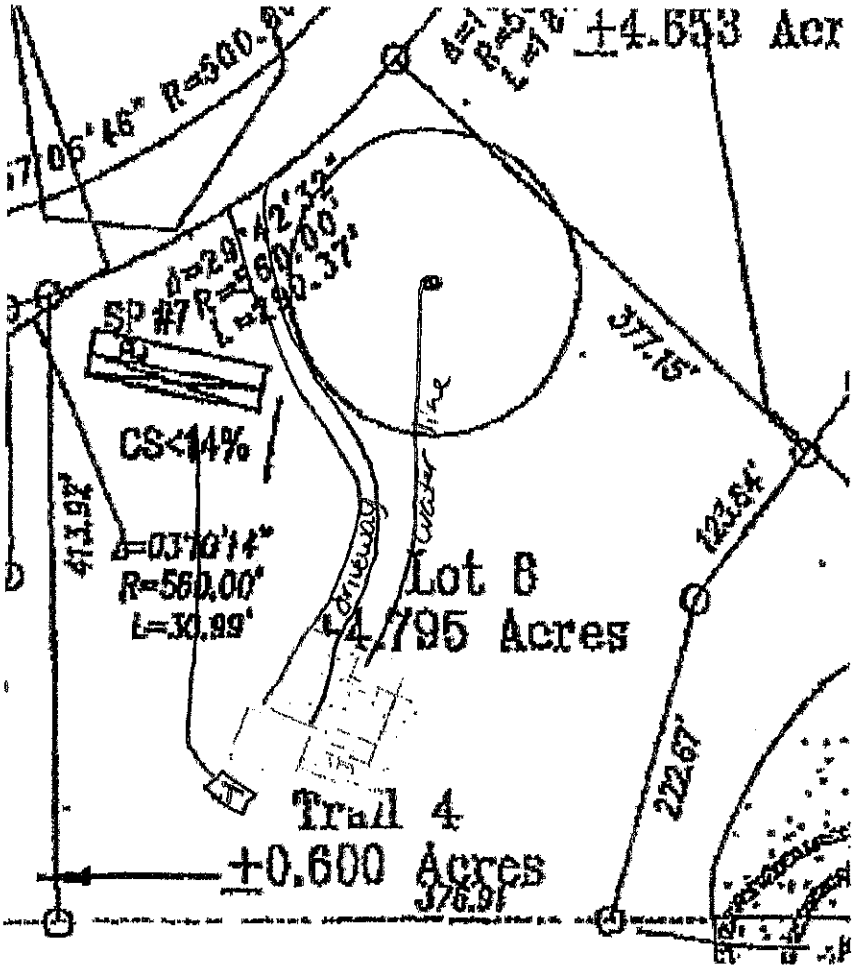
Signed: [signature] *Date:* 2-10-23

X Lincoln County Health Department (LCHD) ____ Licensed Installer w/ approval of LCHD

DISCLAIMER

This permit is not a guarantee by the Department that the system will function properly for a prescribed period of time.

SV


±4.653 Acr
Δ=29°42'32"
R=580.00'
L=300.37'
SP #7
CS<14%
377.15'
123.84'
222.67'
413.92'
Δ=03°10'14"
R=560.00'
L=30.99'
Driveway
Lot 8
4.795 Acres
Trail 4
±0.600 Acres
376.91'
