LINCOLN COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 9/12/2022 Expiration Date: 9/11/2023

Property Owner: Patrick Neild

Mailing Address: [redacted]

Telephone: [redacted] Email:

Installer: Logan Munts License #: 160

Proposed Work: (Check One) ☒ New Installation ☐ Existing System

☐ Replace Drainfield ☐ Replace Tank ☐ Extension

Describe: Pressure dosed system, standard 3' wide trenches

Parcel Description:

Legal: S8 T29N R33W, 78.76 acres

Property Address: Bull Lake Rd, Troy Assessment Code: 6021

Approved Design Criteria:

# of Bedrooms: 4 Septic Tank Size: 1500/500 gallons Drainfield Size: 438 square feet

# of Laterals: 2 Length of Laterals: 73 lineal feet Trench Depth: 24-36 inches

SYSTEM MUST INCLUDE INSTALLATION OF EFFLUENT FILTER AT SEPTIC TANK OUTLET!!

Special Instructions: Install system according to the COSA, lot layout, the Lincoln County Wastewater Treatment and Disposal Regulation, and Circular DEQ-4. CHANGES MUST BE PRE-AUTHORIZED BY THE DEPARTMENT.

Issued By: *Kathi J. Hooper, R.S.*

NOTICE: **The Department must be notified at least 3 business days (72 hours) prior to backfilling the system.** Call 406-283-2442. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation Ch. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.

Closure Statement:

This system is in compliance with the approved design criteria and Lincoln County's Wastewater Treatment and Disposal Regulation.

Signed: Logan Munts *Date:* 9/28/22

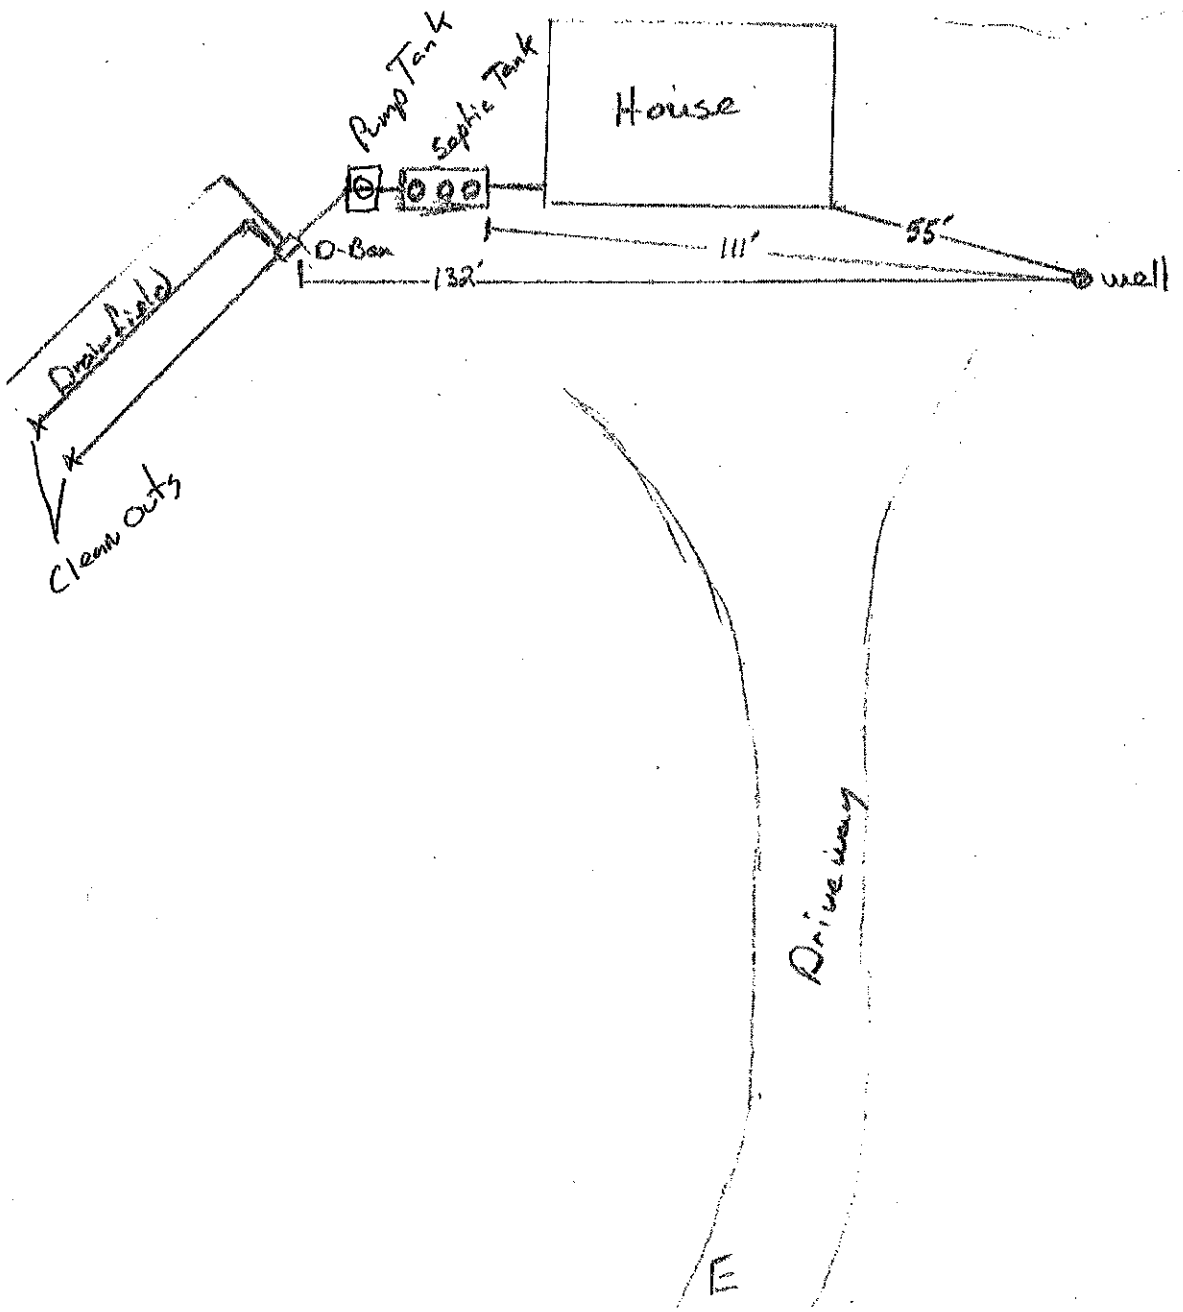
____ Lincoln County Health Department (LCHD) _X_ Licensed Installer w/ approval of LCHD

DISCLAIMER

This permit is not a guarantee by the Department that the system will function properly for a prescribed period of time.

W

LOT LAYOUT


Pump Tank
Septic Tank
House
55'
111'
D-Box
132'
well
S
N
Drainfield
Clean outs
Driveway
E
