LINCOLN COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 04/28/2022 Expiration Date: 04/28/2023

Property Owner: Sanchez-Silva, Olivia c/o: MDS

Address: [redacted]

Telephone: [redacted]

Installer: Dale Schmidt (inspected by MDS) License No. 135

__XX__ New Installation ____ Existing System

____ Repair ____ Replacement ____ Extension ____ Other

Describe: 1,000-gallon septic tank with effluent filter. Gravity feed system with gravelless absorption trenches (infiltration chambers). 3 laterals at 64-feet in length each.

Parcel Description:

Legal: CRYSTAL LAKES UNIT 1, S19, T35 N, R25 W, ACRES 0.659, LOT 34

Address or Location: Crystal Lakes Unit 1, Lot 34

Geo/Assessors code: 0000000731

Approved Design Criteria:

Bedrooms: 2 Septic Tank Size: 1,000 gallon Drainfield Size: 192 Linear Feet

SYSTEM MUST INCLUDE INSTALLATION OF EFFLUENT FILTER AT SEPTIC TANK OUTLET !!

Special Instructions: INSTALL SYSTEM ACCORDING TO LAYOUT, DEQ-4 AND LINCOLN COUNTY WASTEWATER REGULATION #3. ANY DEVIATIONS FROM APPROVED PLAN MUST BE AUTHORIZED BY THE DEPARTMENT.

Issued By: *Nicholas Raines*

Closure Statement:

I, BUCK SCHERMERHORN, have inspected this system and found it to be in compliance with the conditions of the permit, and the Lincoln County Wastewater Treatment and Disposal Regulation.


Signed: Buck Schermerhorn *Date:* 9/23/22

Title: PRESIDENT

NOTICE: The Department must be notified at least 48 business hours prior to backfilling the system. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation No. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.
406-283-2442

DISCLAIMER

This permit is not a guarantee by the Department that the system will function properly for a prescribed period of time.

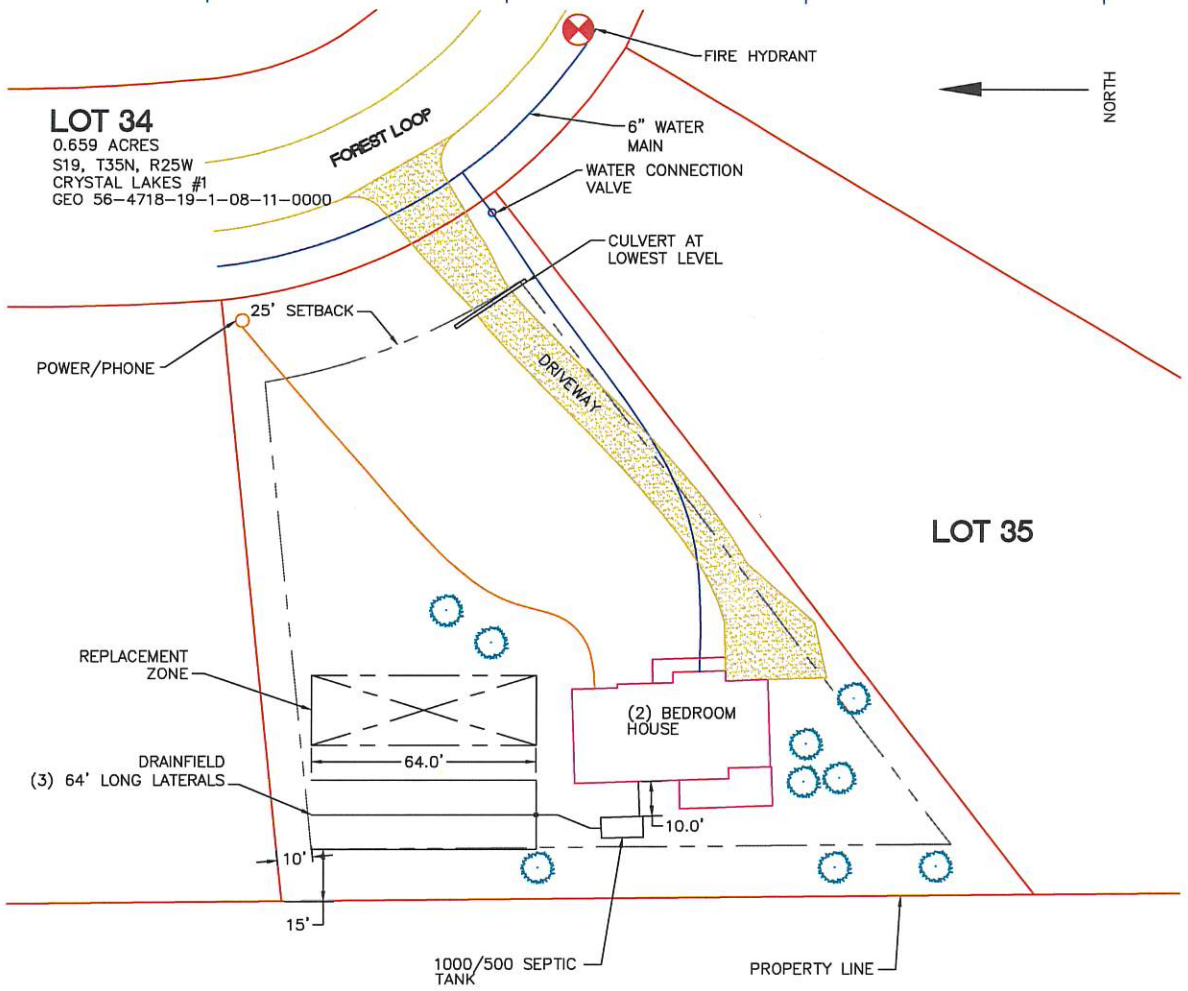

DRAINFIELD SIZING

(2) BEDROOM= 225 GPD
225 GPD/0.5 APP= 450 SQFT
450 SQ FT/2' CHAMBERS= 225 LF
15% DEDUCTION FOR CHAMBERS= 192LF
192 LF/ 3 LATERALS= 64'

OLIVIA SANCHEZ-SILVA SITE LAYOUT

REVISIONS			
REV	DESCRIPTION	BY/DATE	APRD/DATE

REV	DATE	COMPANY	SCALE:	SCHMIDT HAULING & EXCAVATION
		DSHE	1/16 & NOTED	SANCHEZ-SILVA
		CONTRACT:	DATE:	SITE LAYOUT
		VERBAL	3/2022	SCHEMATIC 3/31/22
		PLOT FILE:	WEIGHT	D. SCHMIDT 3/31/22
		PML-0001		402-001 1

THIS DRAWING IS PROPERTY OF SCHMIDT UNTIL CONTRACT HAS BEEN SECURED BETWEEN OWNER & SCHMIDT IT CAN NOT BE SUBMITTED TO ANY OTHER PARTIES WITHOUT WRITTEN APPROVAL FROM MDS MANAGEMENT
