LINCOLN COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 05/06/2025 Expiration Date: 05/05/2026 Permit# 25-60085

Property Owner: Amanda Hunsaker

Mailing Address: [redacted]

Installer: Paul Dalziel License #: 175

Approved Work: (Check One) ☒ New Installation ☐ Existing System

☐ Replace Drainfield ☐ Replace Tank ☐ Extension

Describe: Installation of new pressure dosed system for 1 bedroom House.

Legal: S17, T33 N, R34 W, COS 5005, TRACT 1

Property Address: 505 Stateline Dr., Troy, MT 59935 Assessment Code: 60085

DEQ COSA: E.Q.# 23-2670 Date: 12/29/2023

Approved Design Criteria: Installation of new pressure dosed system for 1 bedroom House with 2 Laterals @ 84' with reduction for chambers.

# of Bedrooms: 1 Septic Tank Size: 1000/500 Trench Width: 36"

# of Laterals: 2 Length of Laterals: 84' Trench Depth: 24"-36"

SYSTEM MUST INCLUDE INSTALLATION OF EFFLUENT FILTER AT SEPTIC TANK OUTLET!!

Special Instructions: Install system according to the lot layout, the Lincoln County Wastewater Treatment and Disposal Regulation, Circular DEQ-4, and COSA(If Applies). Reduction given for chambers. It is the installer's responsibility to ensure that all required horizontal setbacks are met. CHANGES MUST BE PRE-AUTHORIZED BY THE DEPARTMENT.

Issued By: *Robin Blumberg, RS*

NOTICE: The Department must be notified at least 3 business days (72 hours) prior to backfilling the system. Call 406-283-2442. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation Ch. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.

Closure Statement:

This system is in compliance with the approved design criteria and Lincoln County's Wastewater Treatment and Disposal Regulation.

Signed: Robin Blumberg *Date:* 6/23/25

This permit is not finalized until the system is inspected and the closure statement is signed.

This permit is not a guarantee that the system will function properly for a prescribed period of time.

Mandy Hunsaker

DEQ# 23-2670

LINCOLN COUNTY, MONTANA


LOT LAYOUT

HUNSAKER FAMILY TRANSFER
SECTION 17, TWP. 33 N.,
R. 34 W., P.M.M.
FOR: FRANCES HUNSAKER
DATE: JUNE 2023

NO KNOW POTENTIAL SOURCES OF CONTAMINATION WITHIN 500' OF PROPOSED WELLS EXCEPT FOR THE PROPOSED AND EXISTING DRAINFIELDS

NO WELLS OR DRAINFIELDS OR MIXING ZONES WITHIN 100' OF LOT BOUNDRY LINES

PROPOSED BUILDING SITES ARE CONCEPTUAL IN NATURE. THIS LOT LAYOUT IN NO WAY PRESENTS A REGULATORY DOCUMENT FOR PROPOSED BUILDINGS SITES.

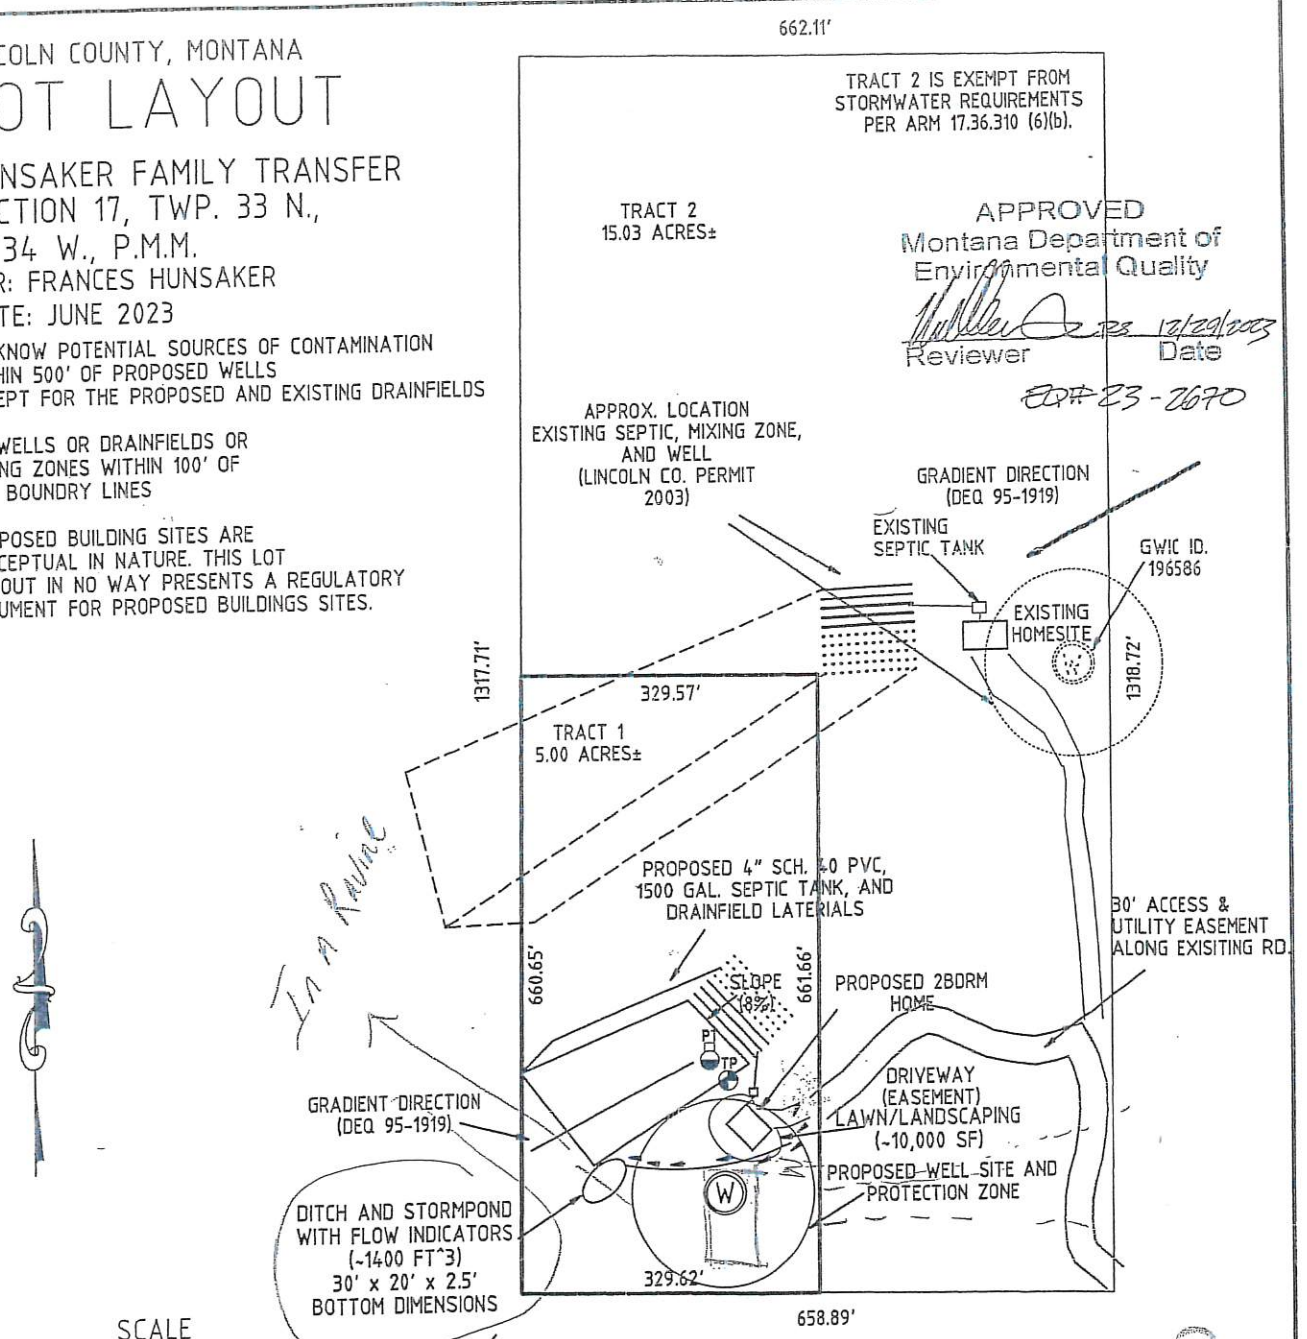

LEGEND

- PROPOSED PRIMARY DRAINFIELD 4-24" X 95' TRENCHES 10' APART
- PROPOSED REPLACEMENT DRAINFIELD 4-24" X 95' TRENCHES 10' APART
- TP / PT — SOIL PROFILE / PERCOLATION SITE
- W — WELL SITE (PROPOSED)
- STORMWATER POND (30' X 20' X 2.5')
- SLOPE

ALL ABSORPTION TRENCHES ARE STANDARD GRAVITY FED; SEE CIRCULAR DEQ 4 FOR TRENCH CONSTURCTION DETAILS

RECEIVED
NOV 30 2023
MT DEQ PUBLIC WATER & SUBDIVISIONS

DAVIS SURVEYING, INC.
TROY, MT. 406.295.5441

DATE: 06/01/2023
DRAWN BY: KD, PhD

FILE: HUNSAKER_LOT_LAYOUT
