LINCOLN COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 10/31/2022 (renewal of 10/19/21 pemit) Expiration Date: 10/30/2023

Property Owner: Tim Orchard

Mailing Address: 120 Nores Ln, Libby, MT

Telephone: [redacted] Email:

Installer: Riley Excavating License #: 147

Approved Work: (Check One) ☒ New Installation ☐ Existing System

☐ Replace Drainfield ☐ Replace Tank ☐ Extension

Describe: Gravity system with standard trenches, chambers

Parcel Description:

Legal: S26 T31N R31W, Tr 1AD6 in S2NESW, 1.00 acres

Property Address: 120 Nores Ln, Libby, MT Assessment Code: 15193

Approved Design Criteria:

# of Bedrooms: 2	Septic Tank Size: 1000 gallons	Trench Width: 24 inches
# of Laterals: 3	Length of Laterals: 64 feet	Trench Depth: 24-36 inches

SYSTEM MUST INCLUDE INSTALLATION OF EFFLUENT FILTER AT SEPTIC TANK OUTLET!!

Special Instructions: Install system according to the lot layout, the Lincoln County Wastewater Treatment and Disposal Regulation, and Circular DEQ-4. 15% reduction given for chambers. ANY CHANGES MUST BE PRE-AUTHORIZED BY THE DEPARTMENT.

Issued By: Kathi J. Hooper, R.S.

NOTICE: The Department must be notified at least 3 business days (72 hours) prior to backfilling the system. Call 406-283-2442. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation Ch. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.

Closure Statement:

I, Jesse Haaa *, have inspected this system and found it to be in compliance with the approved design criteria, Lincoln County's Wastewater Treatment and Disposal Regulation, and the City-County Board of Health for Lincoln County variance approved 1/10/23.*

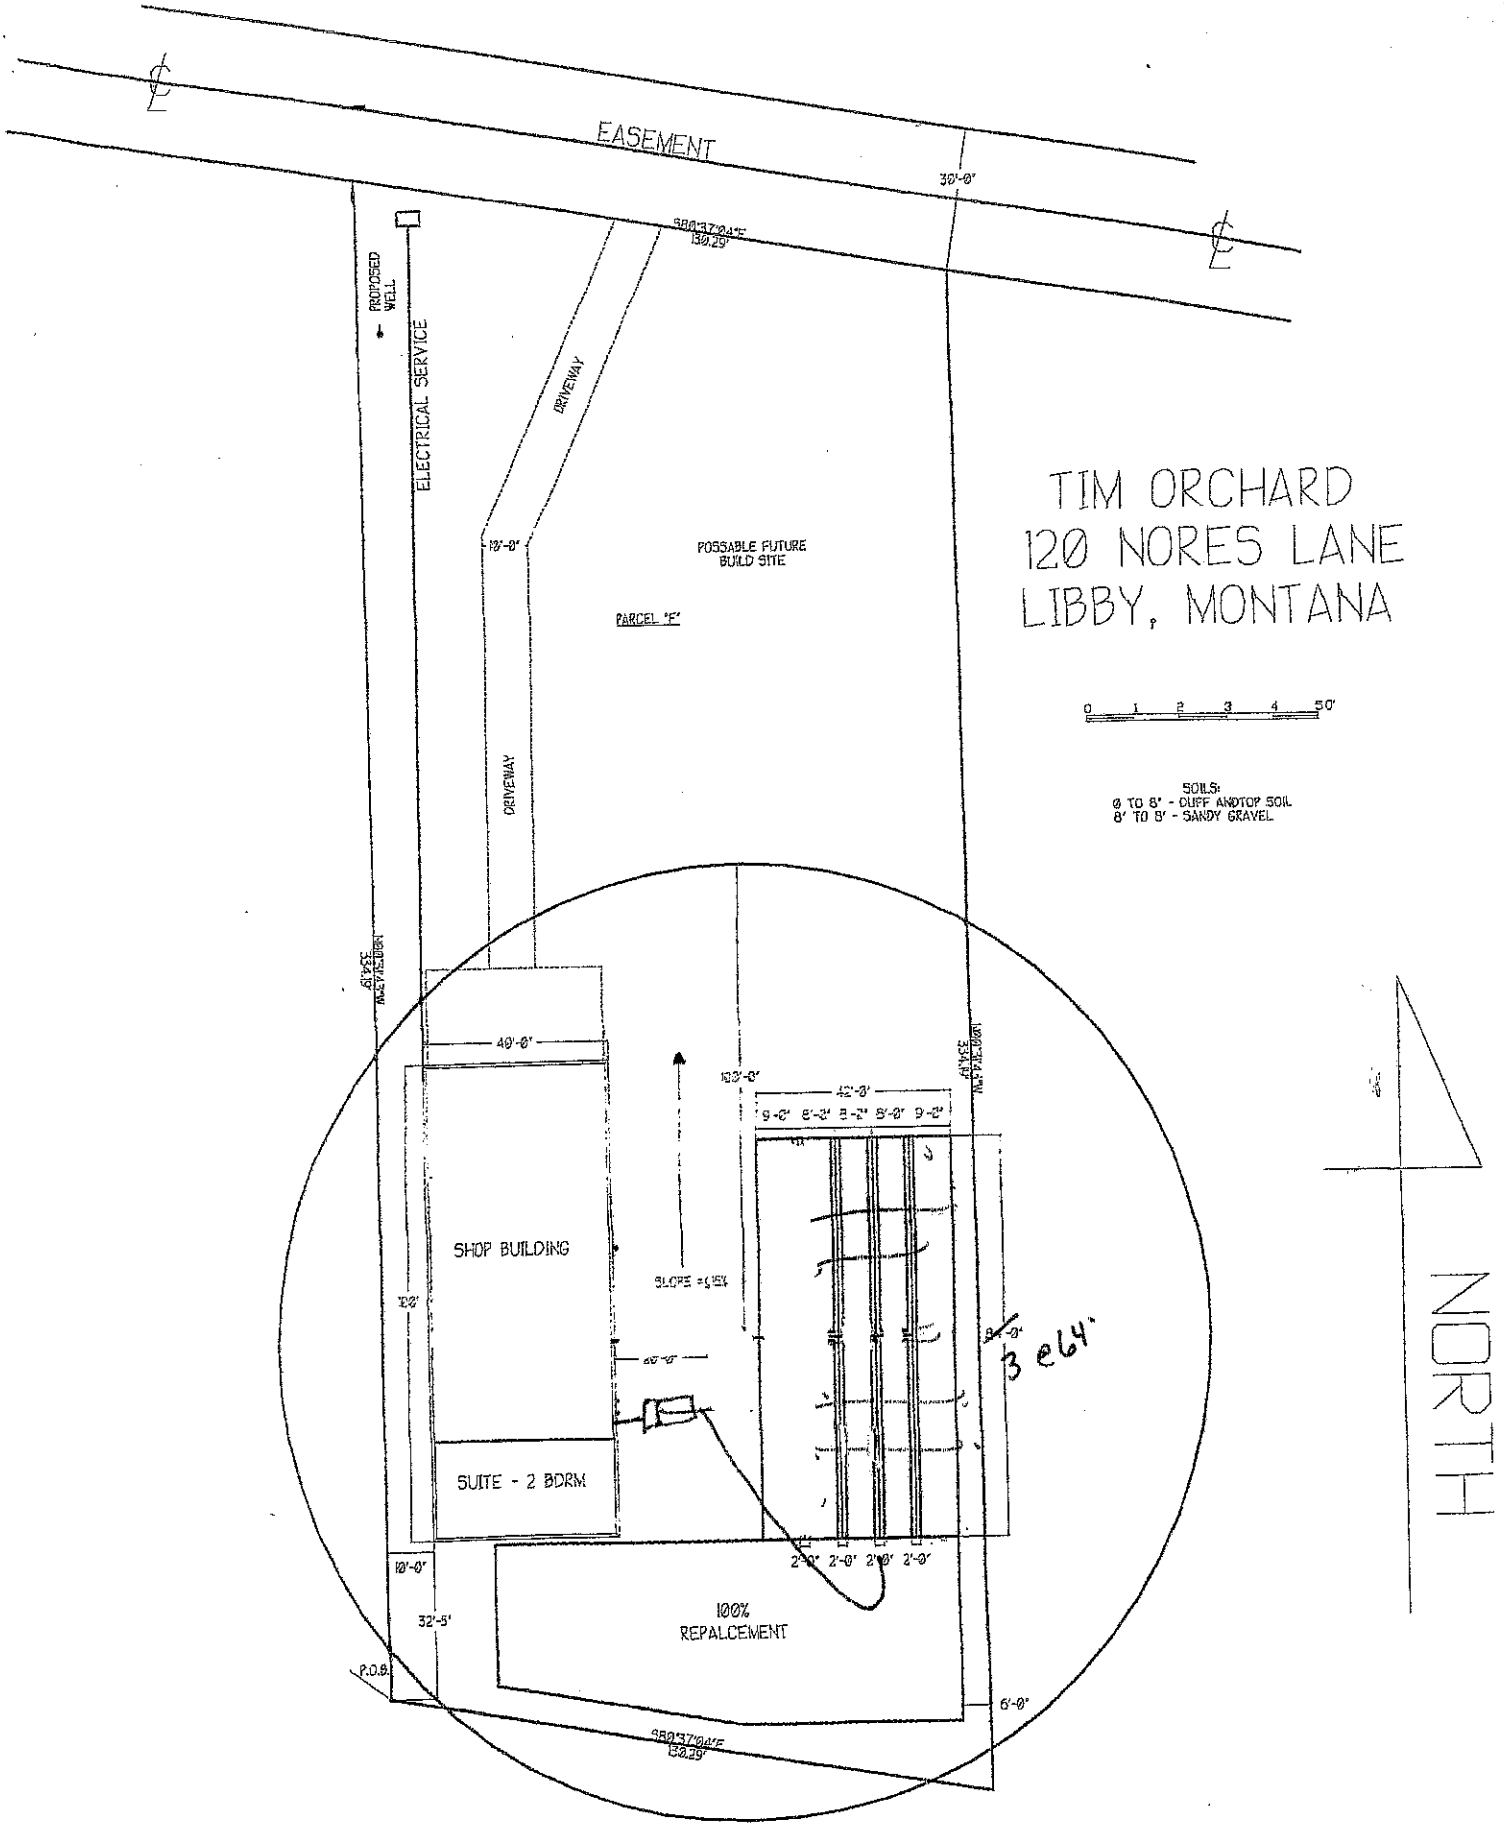
Signed: _____ *Date:* 1-12-23

_√_ Lincoln County Health Department (LCHD) ____ Licensed Installer w/ approval of LCHD

DISCLAIMER

This permit is not a guarantee by the Department that the system will function properly for a prescribed period of time.

SV


EASEMENT
30'-0"
S80°37'04"E
130.29'
PROPOSED WELL
ELECTRICAL SERVICE
DRIVEWAY
10'-0"
POSSABLE FUTURE BUILD SITE
PARCEL "E"
DRIVEWAY
TIM ORCHARD
120 NORES LANE
LIBBY, MONTANA
0 1 2 3 4 50'
SOILS:
0 TO 8' - CLIFF AND TOP SOIL
8' TO 8' - SANDY GRAVEL
N80°37'04"W
534.19'
40'-0"
SHOP BUILDING
SLOPE = 5.15%
103'-0"
42'-0"
9'-0" 8'-2" 8'-2" 8'-0" 9'-2"
N80°37'04"W
534.19'
12'-2"
40'-0"
3 @ 64'
SUITE - 2 BDRM
10'-0"
32'-5"
2'-0" 2'-0" 2'-0" 2'-0"
100%
REPALCEMENT
P.O.B.
6'-0"
S80°37'04"E
130.29'
NORTH

Lincoln City-County Board of Health
418 Mineral Ave
Libby, MT 59923

January 12, 2023

Tim Orchard
c/o Orchard Family Trust
11357 Breithorn Ct
Riverside, CA 92503-0602

RE: Variance Approval

Dear Mr. Orchard,

The City-County Board of Health for Lincoln County voted at their January 10, 2023 meeting to grant you a variance for your wastewater treatment and disposal system which failed inspection on November 3, 2022. This is a variance to the requirement for a minimum separation of at least 5 feet between trench walls of gravity-fed trenches as required in 6.1.3.3 of Circular DEQ 4.

Sincerely,

Amy Fantozzi
Chair

cc: Riley Excavating
