LINCOLN COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH
AFFIDAVIT OF WASTEWATER TREATMENT AND DISPOSAL SYSTEM COMPLIANCE REVIEW FOR SYSTEM INSTALLED, REPAIRED OR REPLACED WITHOUT A VALID PERMIT

Issue Date: 02/02/2022

Property Owner: Robert Stumvoll

Mailing Address: [redacted]

Telephone: [redacted]

Name of Person Who Installed System Being Reviewed: Dan Rogenes

Type of System Work Reviewed:

___ New Installation ____ Existing System

____ Repair ____ Replacement __XX__ Extension ____ Other

Describe: 2 separate 1,000-gallon septic tanks in series. Gravity fed system with infiltrators (chambers). 4 laterals @ 120-feet in length each.

Property Description:

Legal: EDGEWATER ESTATES PH 2, S35, T31 N, R31 W, ACRES 1.076, LOT 16 PM 4936

Address or Location: 700 Airfield Rd. Libby, MT 59923

Assessment Code: 0000014125

Reviewed Design Components:

Wastewater Flows: 400 gpd (5 bedroom) Sewer Lines: Schedule 40 PVS (4")

Septic Tank: Two 1,000-Gallon tanks Effluent Filter: Yes Dosing or Lift Tank: No

Drainfield: 480 Lineal Feet Drainfield Construction: infiltrators Hydraulic Function: yes

Comments:

System Review Documentation Statement:

I, Nicholas Raines, have inspected/reviewed the components of this system as listed above and found it to be in compliance with the sizing, construction, orientation and operating requirements of Chapter 17, Subchapter 36 A.R.M., Circular DEQ-4 and Lincoln County Wastewater Regulation.

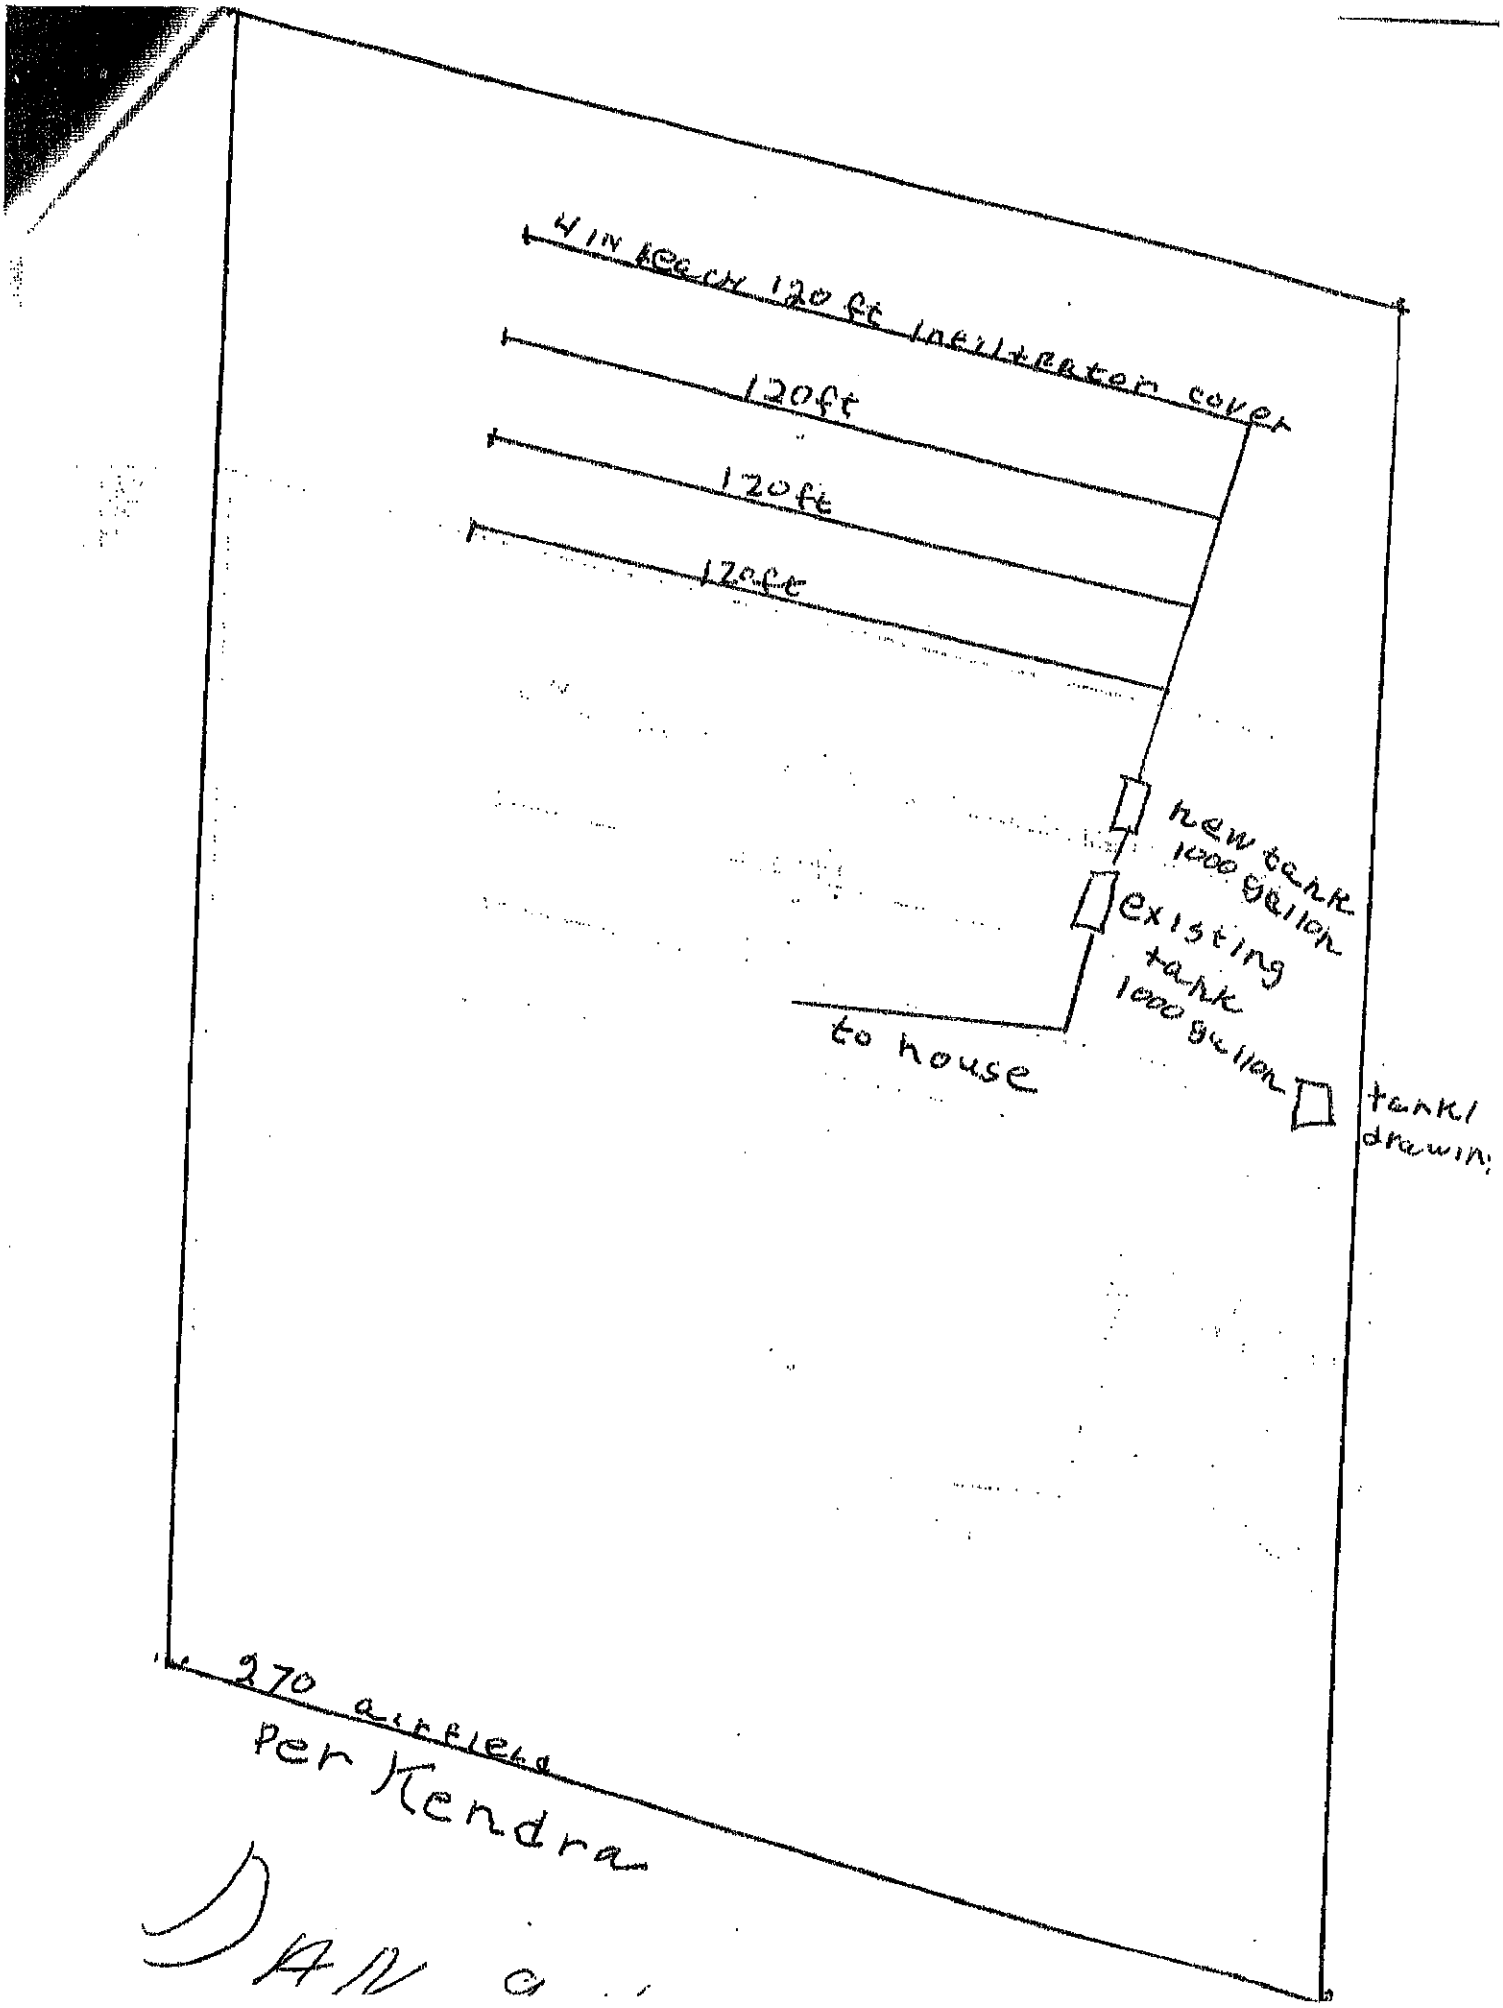
Signed: Nicholas J. Raines *Date:* *02/02/2022*

Title: *Environmental Health Specialist*

NOTICE: This document is not a permit for installation, repair or alterations of a wastewater treatment system. It is merely a statement of affirmation that the Department has conducted an on-site review of an otherwise illegal system and found it to be in compliance with all applicable requirements for that system. This affidavit effectively removes the illegal installation status on this system.

DISCLAIMER

This affidavit of review is not a guarantee by the Department that the system will continue to function properly for any prescribed period of time.


4 in each 120 ft infiltrator cover
120ft
120ft
120ft
new tank
1000 gallon
existing
tank
1000 gallon
to house
tank/
drawin
270 airfield
per Kendra
