LINCOLN COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 7/21/2020 Expiration Date: 07/21/2021

Property Owner: Luke & Samantha Hauke c/o:

Address: [redacted]

Telephone: (Home) [redacted] (Work)

Installer: Tally Hoe License No. 1

Proposed Work: (Check One) ☒ New Installation ☐ Existing System

☐ Repair ☐ Replacement ☐ Extension ☐ Other _____

Describe: Four x 94' Laterals using rockless chamber

Parcel Description:

Legal: S2 T31N R31W, COS 2876, 5.338 acres, Tract 1 in E2NE

Address or Location: 367 Doak Creek Rd, Libby, MT 59923

Approved Design Criteria:

Bedrooms: 2 Septic Tank Size: 1000 gallons Drainfield Size: 376 lineal feet

SYSTEM MUST INCLUDE INSTALLATION OF EFFLUENT FILTER AT SEPTIC TANK OUTLET !!

Special Instructions: INSTALL SYSTEM ACCORDING TO LAYOUT AND LINCOLN COUNTY WASTEWATER REGULATION #3. ANY DEVIATIONS FROM APPROVED PLAN MUST BE AUTHORIZED BY THE DEPARTMENT.

Issued By: *Kathi J. Hooper, R.S.*

Closure Statement:

I, Thomas J Cole *, have inspected this system and found it to be in compliance with the conditions of the permit, and the Lincoln County Wastewater Treatment and Disposal Regulation.*

Signed: Thomas J Cole *Date:* 7-28-20

Title: owner operator

NOTICE: The Department must be notified at least 48 hours prior to backfilling the system. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation No. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.

406-283-2442

SV

EQ#20-1147 Pg 3 of 4


HAUKE RSR

E½ NE¼ S02, T31N, R31W
LINCOLN COUNTY

APPROVED
Montana Department of
Environmental Quality
Reviewer 05/15/2020
Date

Key

- Existing well
- Proposed well
- Proposed D.F. & 100% Replacement Area
- Stormwater Retention Swale (25' x 20' x 2')
- Stormwater flow direction
- Test Hole
- Proposed 1000 gal Septic Tank
- Water Line
- Existing WWTS

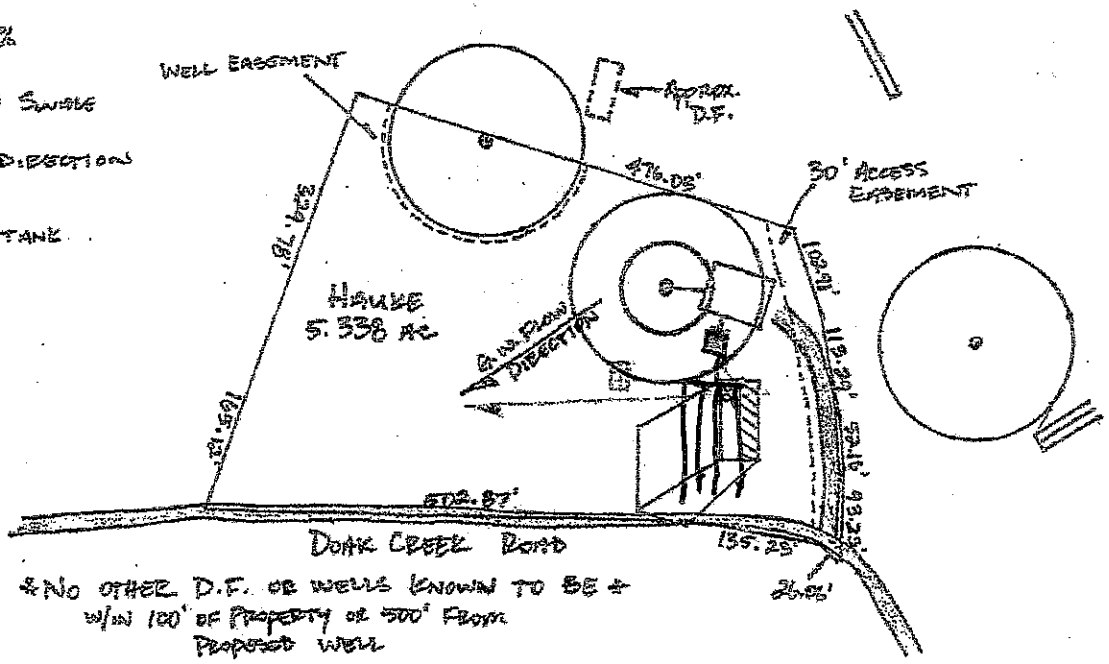

& No other D.F. or wells known to be +
w/in 100' of property or 500' from
proposed well

N
1" = 200'

D. Salisbury Consulting
257 Lupine Dr.
Kalispell, MT 59901
(406) 370-0392
