LINCOLN COUNTY HEALTH DEPARTMENT
ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 08/11//2025 Expiration Date: 08/10/2026 Permit#25-52561

Property Owner: Mark Keenan

Mailing Address: [redacted]

Installer: Licensed Lincoln County Installer License #:

Approved Work: (Check One) ☒ New Installation ☐ Existing System

☐ Replace Drainfield ☐ Replace Tank ☐ Extension

Describe: Installation of new pressure dosed system for 3 Bedroom House.

Legal: DOUBLE CREEK, S17, T30 N, R33 W, LOT 5 ACRES 9.49, PM 6767

Property Address: 176 Double Creek Ln., Troy, MT 59935 Assessment Code: 52561

DEQ COSA: E.Q.# 06-2976 Double Creek Date: 2/27/2007

Approved Design Criteria: Installation of new pressure dosed system for 3 Bedroom House with 4 Laterals @ 99'.

# of Bedrooms: 3 Septic Tank Size: 1000/500 Trench Width: 36"

# of Laterals: 4 Length of Laterals: 99' Trench Depth: 24"-36"

SYSTEM MUST INCLUDE INSTALLATION OF EFFLUENT FILTER AT SEPTIC TANK OUTLET!!

Special Instructions: Install system according to the lot layout, the Lincoln County Wastewater Treatment and Disposal Regulation, Circular DEQ-4, and COSA(If Applies). It is the installer's responsibility to ensure that all required horizontal setbacks are met. CHANGES MUST BE PRE-AUTHORIZED BY THE DEPARTMENT.

Issued By: *Robin Blumberg, RS*

NOTICE: The Department must be notified at least 3 business days (72 hours) prior to backfilling the system. Call 406-283-2442. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation Ch. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.

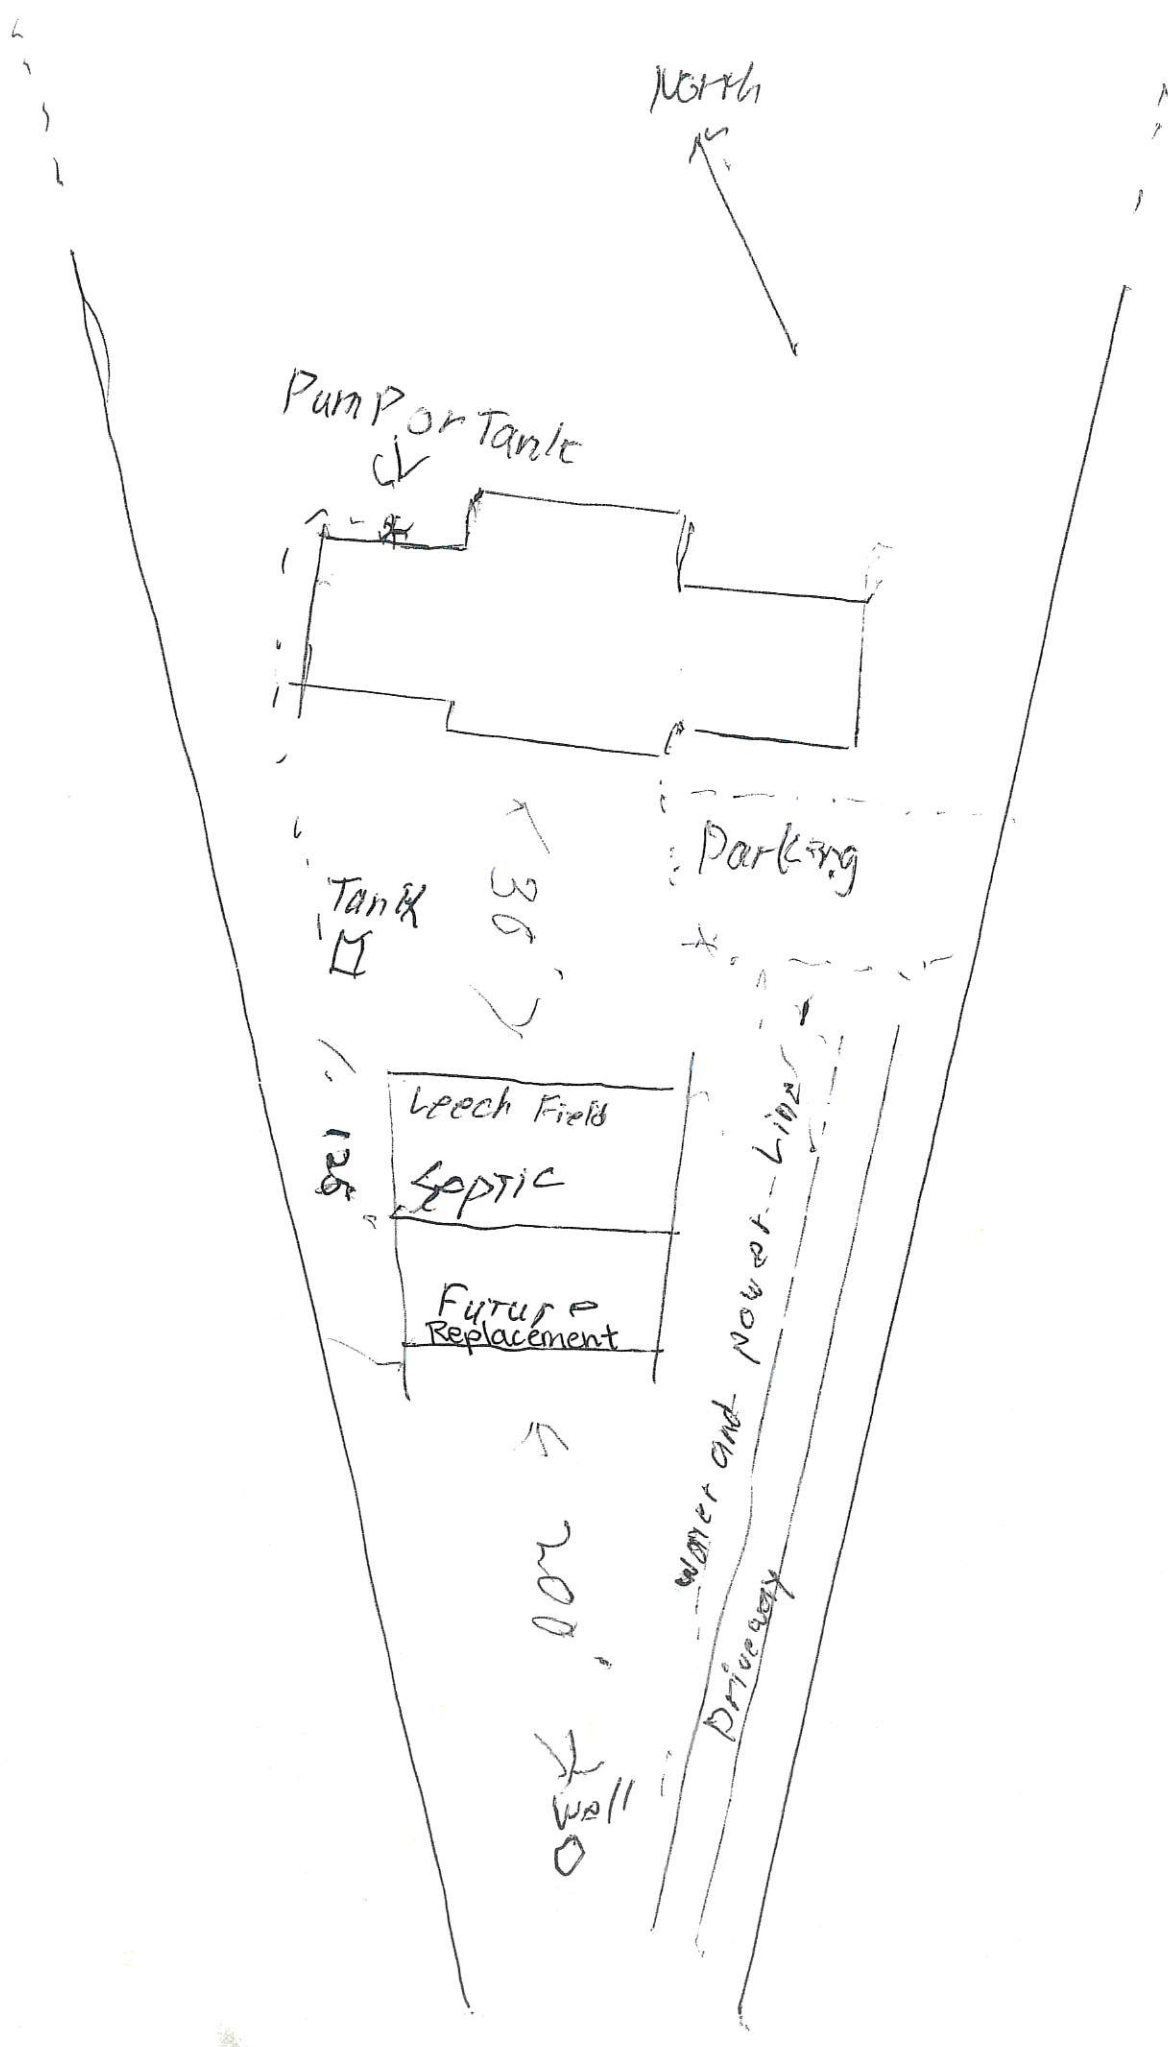
Closure Statement:

This system is in compliance with the approved design criteria and Lincoln County's Wastewater Treatment and Disposal Regulation.

Signed: _____ *Date:* _____

This permit is not finalized until the system is inspected and the closure statement is signed.

This permit is not a guarantee that the system will function properly for a prescribed period of time.


North
Pump or Tank
Parking
Tank
30'
Leech Field
Septic
Future Replacement
125'
100'
Well
Power and Sewer Lines
Driveway
