LINCOLN COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 5/12/2020 Expiration Date: 5/12/2021

Property Owner: Patrick Morey c/o:

Address: [redacted]

Telephone: (Home) [redacted] (Work)

Installer: Thompson Contracting Inc (TCI) License No. 73

__xx__ New Installation ____ Existing System

____ Repair ____ Replacement ____ Extension ____ Other

Describe: Three 65' laterals using drain rock and perf pipe.

Parcel Description:

Legal: S23 T30 R31 COS 2294 Parcel B

Address or Location: 150 Darsow Road

Geo/Assessors code: 0000052416

Approved Design Criteria:

Bedrooms 3 Septic Tank Size: 1000 gallons Drainfield Size: 195 lineal feet

SYSTEM MUST INCLUDE INSTALLATION OF EFFLUENT FILTER AT SEPTIC TANK OUTLET !!

Special Instructions: INSTALL SYSTEM ACCORDING TO LAYOUT, DEQ-4 AND LINCOLN COUNTY WASTEWATER REGULATION #3. ANY DEVIATIONS FROM APPROVED PLAN MUST BE AUTHORIZED BY THE DEPARTMENT.

Issued By: Jake Mertes, R.S.

Closure Statement:

I, Levi Thompson *, have inspected this system and found it to be in compliance with the conditions of the permit, and the Lincoln County Wastewater Treatment and Disposal Regulation.*

Signed: [signature] *Date:* 5/22/20

Title: Vice President of TCI

NOTICE: The Department must be notified at least 48 hours prior to backfilling the system. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation No. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.


406-283-2442

DISCLAIMER

This permit is not a guarantee by the Department that the system will function properly

SITE PLAN DARSOW
BOUNDARY ADJUSTMENT
NW 1/4 NE 1/4 SEC 23
T30N, R31W, P.M.M.
LINCOLN COUNTY, MONTANA

NTS

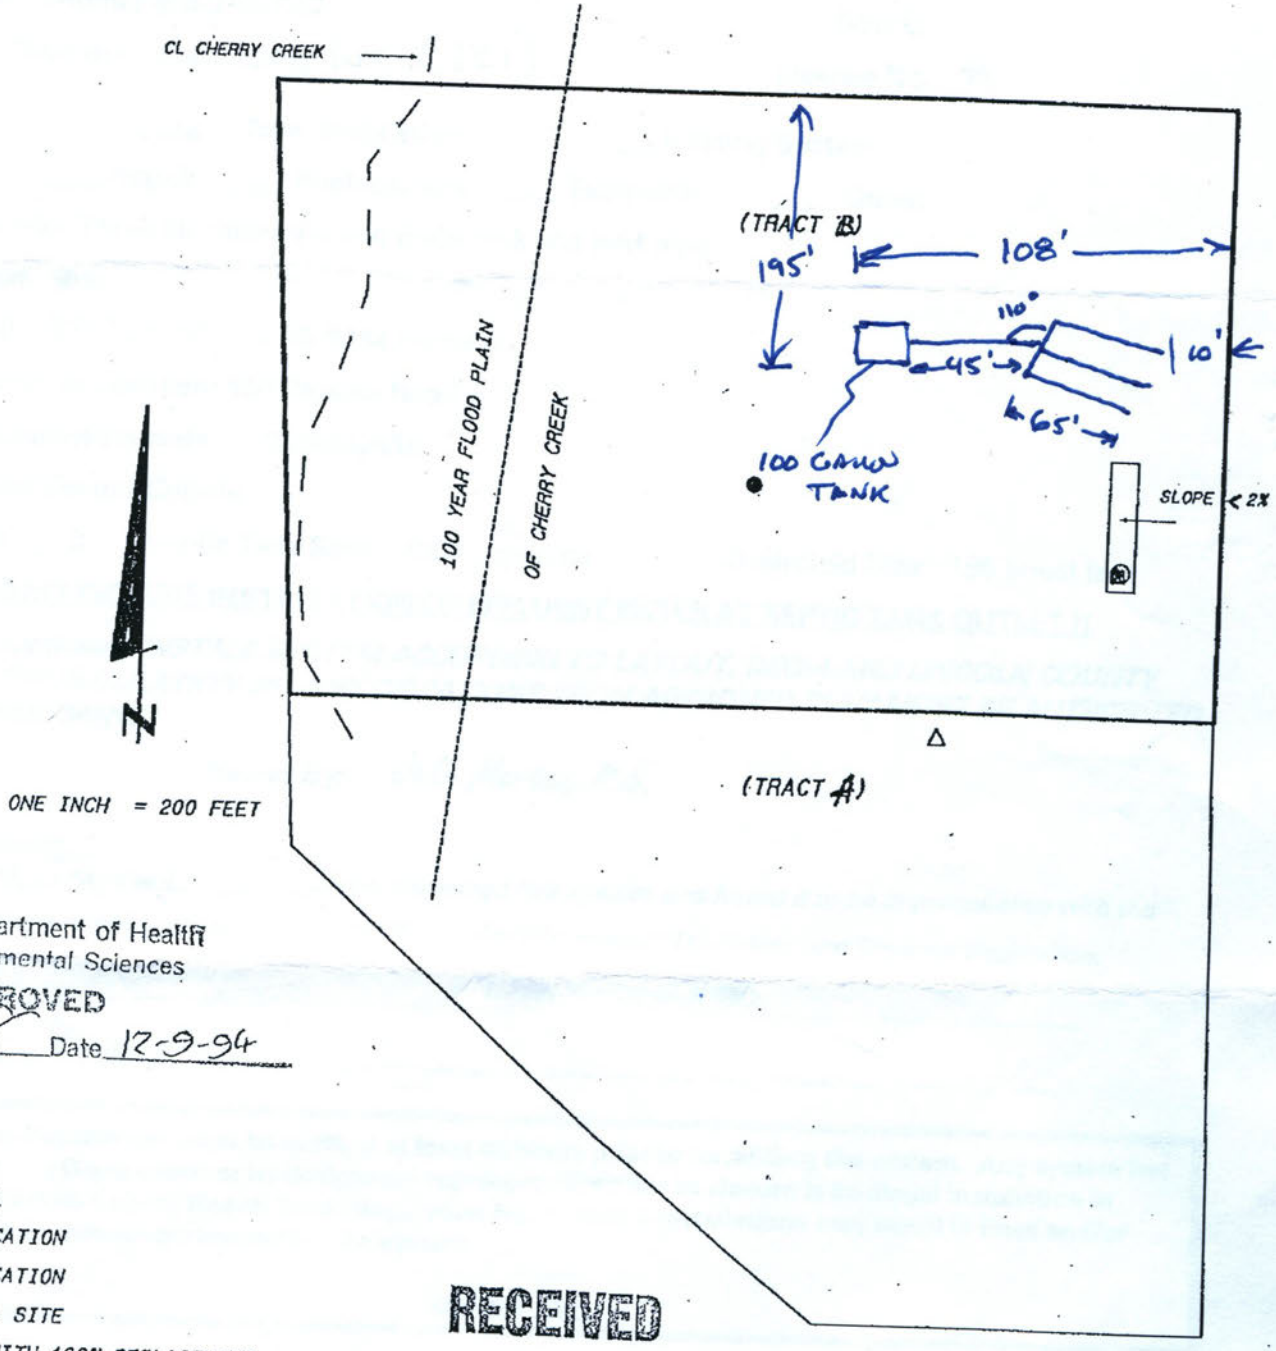

Montana Department of Health
and Environmental Sciences
APPROVED
Initials [illegible] Date 12-9-94

LEGEND

- △ EXISTING WELL
- ⊠ SOIL TEST LOCATION
- ⊙ PERC TEST LOCATION
- ● PROPOSED WELL SITE
- ▯ DRAIN FIELD WITH 100% REPLACEMENT

RECEIVED
DEC 0 1 1994
MONTANA
DEPT. OF HEALTH & ENV. SCIENCES
WATER QUALITY BUREAU
