LINCOLN COUNTY
DEPARTMENT OF ENVIRONMENTAL HEALTH
WASTEWATER TREATMENT AND DISPOSAL SYSTEM PERMIT

Issue Date: 7/9/2018 Expiration Date: 7/9/2019

Property Owner: Gary Pulford c/o:

Address: [redacted]

Telephone: (Home) [redacted] (Work)

Installer: Self License No.

__xx__ New Installation ____ Existing System

____ Repair ____ Replacement ____ Extension ____ Other

Describe: Two 65' pressure dosed sand-lined laterals.

Parcel Description:

Legal: S03 T35 R32

Address or Location: Flamingo Subdivision Lot 1 101 Redband Road., Troy

Geo/Assessors code: 0000000308

Approved Design Criteria:

Bedrooms 2 Septic Tank Size: 1000/500 gallons Drainfield Size: 130 Linear Feet

SYSTEM MUST INCLUDE INSTALLATION OF EFFLUENT FILTER AT SEPTIC TANK OUTLET !!

Special Instructions: INSTALL SYSTEM ACCORDING TO LAYOUT, DEQ-4 AND LINCOLN COUNTY WASTEWATER REGULATION #3. ANY DEVIATIONS FROM APPROVED PLAN MUST BE AUTHORIZED BY THE DEPARTMENT.

Issued By: Jake Mertes, R.S.

Closure Statement:

I, Jake Mertes *, have inspected this system and found it to be in compliance with the conditions of the permit, and the Lincoln County Wastewater Treatment and Disposal Regulation.*

Signed: _____ *Date:* 9/10/2018

Title: County Sanitarian

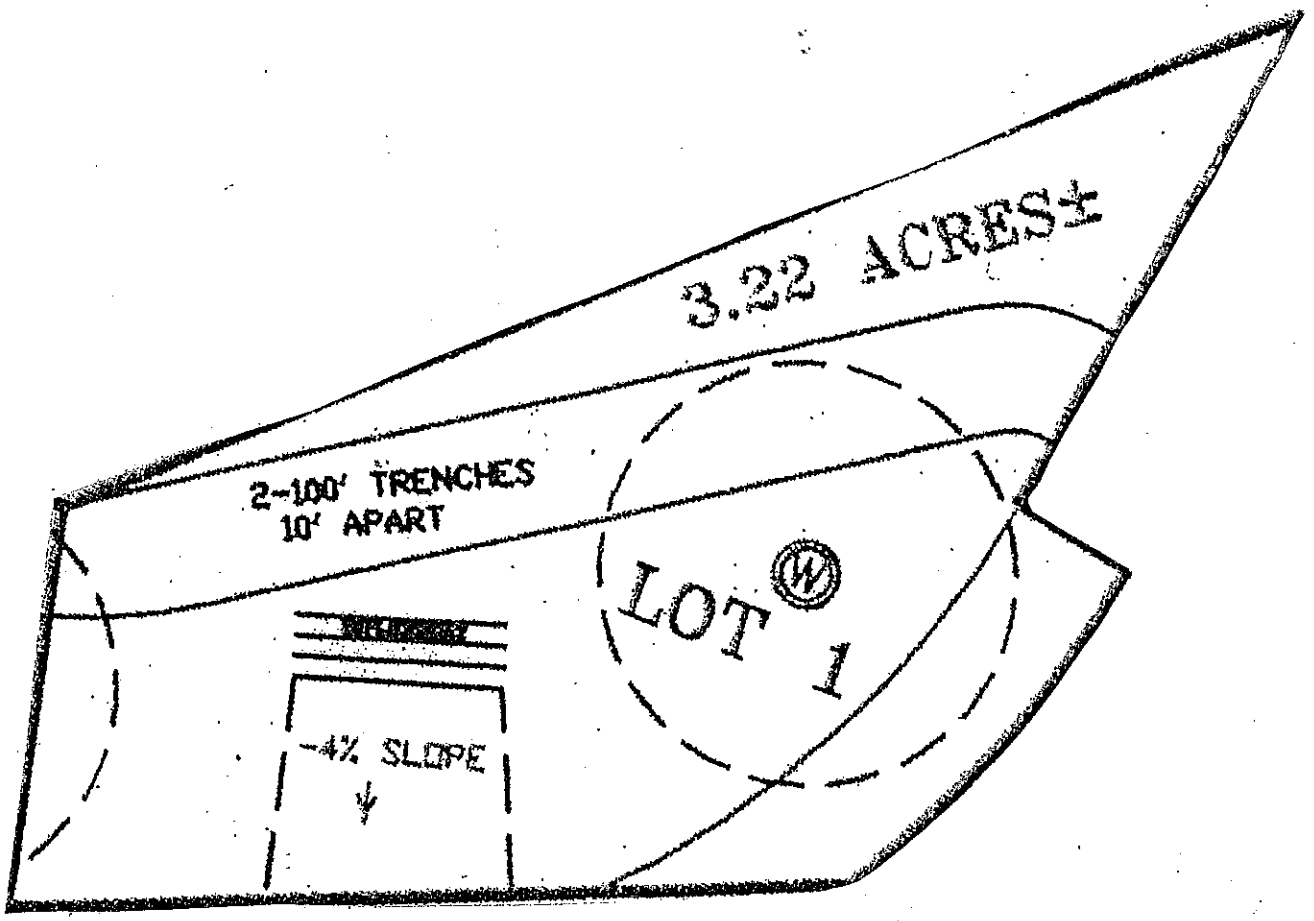
NOTICE: The Department must be notified at least 48 hours prior to backfilling the system. Any system not inspected by the Department or its designated representative prior to closure is an illegal installation in violation of Lincoln County Health Board Regulation No. 3. Illegal installations may result in fines and/or requirements to remove or reconstruct the system.

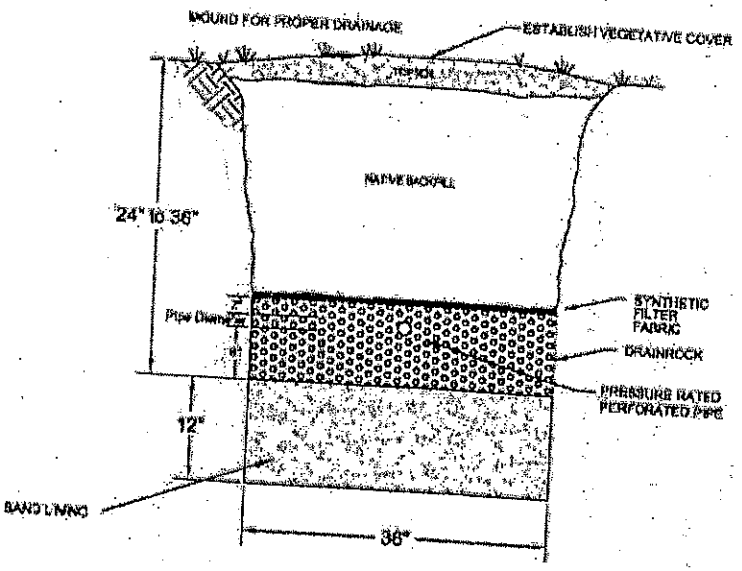
406-283-2442

DISCLAIMER

This permit is not a guarantee by the Department that the system will function properly for a prescribed period of time.

LOT LAYOUT


3.22 ACRES±
2-100' TRENCHES
10' APART
LOT 1
4% SLOPE


MOUND FOR PROPER DRAINAGE
ESTABLISH VEGETATIVE COVER
TOPSOIL
NATIVE BACKFILL
24" TO 36"
Pipe Diameter
SYNTHETIC FILTER FABRIC
DRAINROCK
PRESSURE RATED PERFORATED PIPE
12"
SAND LINING
36"
